

- 1. This plan is submitted to fulfill the woodland conservation requirements for grading permit.

 2. Cutting or clearing of woodland not in conformance with this plan or without the expressed
- written consent of the Planning Director or designee shall be subject to a \$9.00 per square foot mitigation fee.
- 3. A pre-construction meeting is required prior to the issuance of grading permits. The Department of Permiting, Inspections and Enforcement shall be contacted prior to the start of any work on the site to conduct a pre-construction meeting where implementation of woodland conservation measures shown on this plan will be discussed in detail.
- 4. The developer or builder of the lots or parcels shown on this plan shall notify future buyers of any woodland conservation areas through the provision of a copy of this plan at time of contract signing. Future property owners are also subject to this requirement.
- signing. Future property owners are also subject to this requirement.

 5. The owners of the property subject to this tree conservation plan are solely responsible for
- conformance to the requirements contained herein.

 6. The property is within the Rural Tier and is zoned OS
- 7. The site is not adjacent to a roadway designated as scenic, historic, a parkway or a scenic
- 8. The site is not adjacent to a roadway classified as arterial or greater.
- 9. This plan is grandfathered under CB-27-2010, Section 25-117(g).
- 10. <u>Tree Preservation and Retention Notes</u>
 a. All woodlands designated on this plan for preservation are the responsibility of the property owner. The woodland areas shall remain in a natural state. This includes the canopy trees and understory vegetation. A revised tree conservation plan is required prior to clearing woodland areas that are not specifically identified to be cleared on the approved TCP2.
- b. Tree and woodland conservation methods such as root pruning shall be conducted as noted on this plan.
- c. The location of all temporary tree protection fencing (TPFs) shown on this plan shall be flagged or staked in the field prior to the pre-construction meeting. Upon approval of the
- locations by the county inspector, installation of the TPF's may begin.

 d. All temporary tree protection fencing required by this plan shall be installed prior to commencement of clearing and grading of the site and shall remain in place until the bond is released for the project. Failure to install and maintain temporary or permanent tree protective devices is a violation of this TCP2.
- e. Woodland preservation areas shall be posted with signage as shown on the plans at the same time as the temporary TPF installation. These signs must remain in perpetuity.

 Movel of Hazardous Trees or Limbs by Developers or Builders
- Removal of Hazardous Trees or Limbs by Developers or Builders

 f. The developer and/or builder is responsible for the complete preservation of all forested areas shown on the approved plan to remain undisturbed. Only trees or parts thereof
- designated by the county as dead, dying, or hazardous may be removed.

 g. A tree is considered hazardous if a condition is present which leads a Certified Arborist or Licensed Tree Expert to believe that the tree or a portion of the tree has a potential to fall and strike a structure, parking area, or other high use area and result in personal
- injury or property damage.

 h. During the initial stages of clearing and grading, if hazardous trees are present, or trees are present that are not hazardous but are leaning into the disturbed area, the permitee shall remove said trees using a chain saw. Corrective measures requiring the removal of the hazardous tree or portion thereof shall require authorization by the county inspector. Only after the approval by the inspector may the tree be cut by chain saw to near the existing round level. The stump shall not be removed or covered with soil, mulch, or other materials that would inhibit sprouting.
- i. If a tree or trees become hazardous prior to bond release for the project, due to storm events or other situations not resulting from an action by the permitee, prior to removal a Certified Arborist or a Licensed Tree Expert must certify that the tree or the portion of the tree in question has a potential to fall and strike a structure, parking area, or other high use area and may result in personal injury or property damage. If a tree or portions thereof are in imminent danger of striking a structure, parking area, or other high use area and may result in personal injury or property damage then the certification is not required and the permitee shall take corrective action immediately. The condition of the area shall be fully documented through photographs prior to corrective action being taken. The photos shall be submitted to the inspector for documentation of the damage.

11. If corrective pruning may alleviate a hazardous condition, the Certified Arborist or a Licensed Tree Expert may proceed without further authorization. The pruning must be done in accordance with the latest edition of the appropriate ANSI A—300 Pruning Standards. The condition of the area shall be fully documented through photographs prior to corrective action being taken. The photos shall be submitted to the inspector for documentation of the damage.

12. Debris from the tree removal or pruning that occurs within 35 feet of the woodland edge may be removed and properly disposed of by recycling, chipping, or other acceptable methods. All debris that is more than 35 feet from the woodland edge shall be cut up to allow contact with the ground, thus encouraging decomposition. The smaller materials shall be placed into brush piles that will serve as wildlife habitat.

13. Tree work to be completed within a road right—of—way requires a permit from the Maryland Department of Natural Resources unless the tree removal is shown within the approved limits of disturbance on a TCP2. The work is required to be conducted by a Licebsed Tree Expert.

14. When Virigina Pines are present within 40 feet of the limits of disturbance in a preservation

- a. The subject property contains Virginia Pines (Pinus virginiana) that are subject to wind throw. All Virginia pines greater than 6 inches in diameter within 40 feet of the final proposed limit of disturbance or the boundary of the property shall be cut down by hand during the clearing of the site.
- b. After the Virginia pines have been removed, the contractor responsible for implementation of this TCP2 shall submit an evaluation of the stocking levels for the residual stand, management techniques to be applied to the residual stand, and supplemental planting requirements to the M-NCPPC Planning Department. This evaluation shall be submitted prior to the issuance of the first building permit to ensure that all high risk trees have been removed. A planting schedule and/or details for the management of natural regeneration to fully restock the site must be shown on the plan.

15. POST DEVELOPMENT NOTES

conservation area is not permitted.


When woodlands and/or specimen, historic or champion trees are to remain:

a. If the developer or builder no longer has an interest in the property and the new owner desires to remove a hazardous tree or portion thereof, the new owner shall obtain a written statement from a Certified Arborist or Licensed Tree Expert identifying the hazardous condition and the proposed corrective measures prior to having the work conducted. After proper documentation has been completed per the handout "Guidance for Prince George's County Property Owners, Preservation of Woodland Conservation Areas", the arborist or tree expert may then remove the tree. The stump shall be cut as close to the ground as possible and left in place. The removal or grinding of the stumps in the woodland

16. If a tree or portions thereof are in imminent danger of striking a structure, parking area, or other high use area and may result in personal injury or property damage then the certification is not required and the permitee shall take corrective action immediately. The condition of the area shall be fully documented through photographs prior to corrective action being taken. The photos shall be submitted to the inspector for documentation of the damage.


17. Tree work to be completed within a road right—of—way requires a permit from the Maryland Department of Natural Resources unless the tree removal is shown within the approved limits of disturbance on a TCP2. The work is required to be conducted by a Licensed Tree Expert.


- b. The removal of noxious, invasive, and non-native plant species from any woodland preservation area shall be done with the use of hand-held equipment only (pruners or a chain saw). These plants may be cut near the ground and material less than two inches diameter may be removed from the area and disposed of appropriately. All material from these noxious, invasive, and non-native plants greater than two (2) inches diameter shall be cut to allow contact with the ground, thus encouraging decomposition.
- c, The use of broadcast spraying of herbicides is not permitted. However, the use of herbicides to discourage re-sprouting of invasive, noxious, or non-native plants is permitted if done as an application of the chemical directly to the cut stump immediately following cutting of plant tops. The use of any herbicide shall be done in accordance with the label instructions
- d. The use of chainsaws is extremely dangerous and should not be conducted with poorly maintained equipment, without safety equipment, or by individuals not trained in the use of this equipment for the pruning and/or cutting of trees.

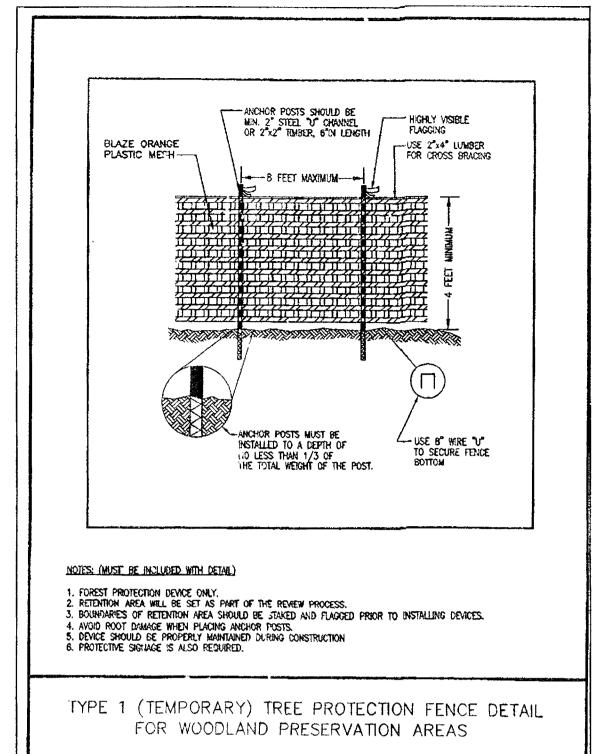

August 2010

A-4. DET-4

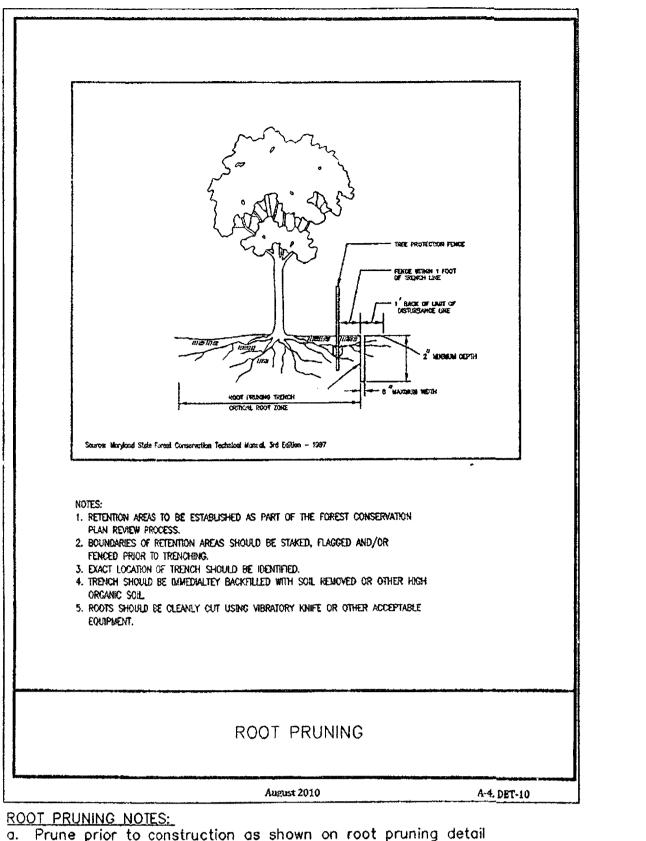

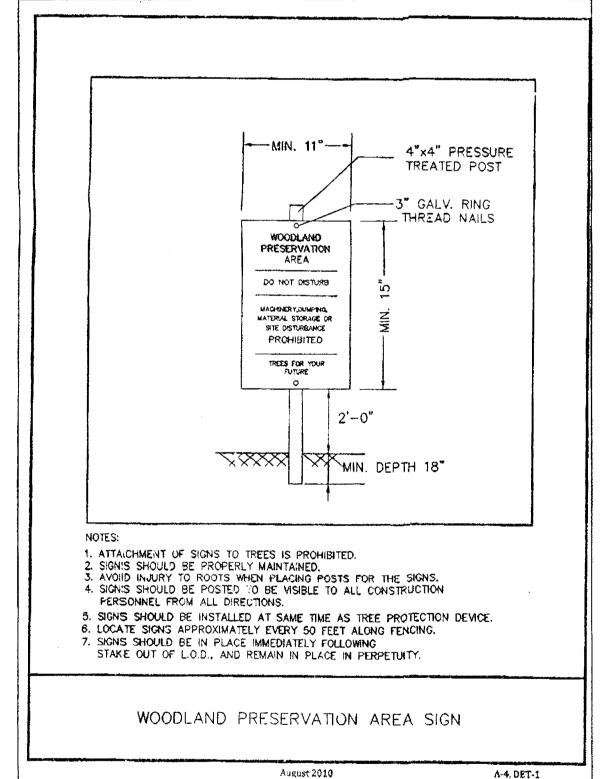

Prune root with a clean cut using proper pruning equipment

or other suitable material

in advance of construction

e. Monitor for signs of stress

Exposed roo's should be covered immediately with topsoil, peat moss,

d. For trees over 15" diameter, root pruning may be done up to one year

M-NCPPC
Prince George's Planning Department
Environmental Planning Section

APPROVAL
TREE CONSERVATION PLAN

TCP2-004-14

Approved by

Date

O1

MM72, 2014

O2

O3

O4

O5

SINGLE LOT TCP2 WITH PREVIOUSLY APPROVED TCP1 WOODLAND CONSERVATION WORKSHEET FOR PRINCE GEORGE'S COUNTY

| 1 | ZONE | 0-8 | | | | | | | |
|----|---|--|------|-------------|---------------|--|---------------------|------------|--|
| 2 | GROSS TRACT | 5.02 | | | | | | | |
| 3 | FLOODPLAIN | 0.00 | | | | | | | |
| 4 | PREVIOUSLY DEDICATED LAND | 0.00 | | | | | | | |
| 5 | NET TRACT (NTA) | 5.02 | | | | | | | |
| 6 | PROPERTY DESCRIPTION OR SUBDIVISION NAME | KNOTT SUBIDIVISION LOT 4 | | | | | | | |
| 7 | OWNER | CONSTANCE J. CHRISTIAN & WILLIAM V. HAMILTON | | | | | | | |
| 8 | ADLRESS | 23330 MECK ROAD, AQUASCO MD 20 | | | O MD 20608 | | | | |
| 9 | PHONE | 301-752- | 0800 | | | | | | |
| 10 | PREVIOUS TOP1 NUMBER | 1-049-0 | 4 | | | | | | |
| | WOODLAND CONSERVATION CALCULATIONS | | | | | NET TRACT | | FLOODPLAIN | |
| | | | | | | (ACRES) | | (ACRES) | |
| | | | | | | 4.97 | 1 | 0.00 | |
| 11 | ACREAGE OF EXISTING WOODLAND | | | | 54.18% | 2.72 | | 0.00 | |
| 12 | WOODLAND CONSERVATION REQUIRED FOR LOT PER TCP1 | | | | 34.10% | 0.88 | | 0.00 | |
| 13 | AREA OF WOODLAND CLEARED PER TCP1 | | | | | 1.14 | | 0.00 | |
| 14 | AREA OF WOODLAND CLEARED PER TCP2 | | | <u> </u> | | 2.50 | | 0.00 | |
| 15 | | | | <u> </u> | | 2.50 | | 0.00 | |
| 16 | ADDITIONAL WOODLAND CLEARED BY TCP2 | | 0.2 | | | | | 0.00 | |
| 17 | | | N | | | 4 DED! 400 /FVE | DEDLACEVENT RECURED | | |
| 18 | | | 1.1 | | | | | 0.29 | |
| 19 | CLEARING DELON WOT | | | X) A | DOITIONAL 2:1 | البدائدة التركيب المراجعة الم | QUIKED | 0.00 | |
| 20 | TOTAL WOODLAND CONSERVATION REQUIRED FOR | R THIS LOT | | | | 2.79 | | | |
| | | | | · | | (40050) | | | |
| 21 | WOODLAND CONSERVATION PROVIDED | | | | (ACRES) | | | | |
| 22 | WOODLAND PRESERVATION | | | | | 2.83 | | | |
| 23 | REFORESTATION/REPLACEMENT | | | | | 0.00 | | | |
| 24 | AFFORESTATION | | | | | 0.00 | - | | |
| 25 | AREA APPROVED FOR FEE-IN-LIEU | | | | | 0.00 | - | | |
| 26 | | | | | | 0.00 | | | |
| _ | | | | | | 1 .0.00 | 1 | | |

 29 AREA OF NET TRACT WOODLAND NOT CLEARED
 3.83

 30 WOODLAND RETAINED NOT PART OF REQUIREMENTS
 1.00

27 OFF-SITE MITIGATION PROVIDED ON THIS PROPERTY

23 TOTAL WOODLAND CONSERVATION PROVIDED

PROPERTY OWNERS AWARENESS CERTIFICATE

I/WE CONSTANCE J. CHRISTIAN AND WILLIAM V. HAMILTON HEREBY ACKNOWLEDGE THAT WE ARE AWARE OF THIS TYPE 2 TREE CONSERVATION PLAN (TCP2) AND THAT WE UNDERSTAND THE REQUIREMENTS AS SET FORTH IN THIS TCP2.

DATE


WILLIAM V. HAMILTON

DATE

WOODLAND CONSERVATION PLAN PREPARED BY JOHN F. HILLEY, RLA

23330 NECK ROAD

SHEET 2 OF 2



SURVEYS

Established 1975

3140 WEST WARD ROAD SUITE 103

DUNKIRK, MARYLAND 20764

410-288-9712 1-800-235-4681

FAX: 410-286-9716

TYPE 2 TREE CONSERVATION PLAN

LOT 4 KNOTT SUBDIVISION

EIGHTH DISTRICT
PRINCE GEORGE'S COUNTY, MARYLAND

DRAWN BY:

SCALE: 1" = 40' DESIGNED BY:

DATE: 9/2013
