TREE CONSERVATION PLAN TYPE 2
EZ STORAGE COLLEGE PARK

5151 BRANCHVILLE ROAD
COLLEGE PARK, MARYLAND
BERWIN (21ST) ELECTION DISTRICT, PRINCE GEORGE'S COUNTY

GENERAL NOTES

1. THIS PLAN IS SUBMITTED TO FULFILL THE WOODLAND CONSERVATION REQUIREMENTS FOR DSP-15031.

2. CUTTING OR CLEARING OF WOODLAND NOT IN CONFORMANCE WITH THIS PLAN OR WITHOUT THE EXPRESSED WRITTEN CONSENT OF THE PLANNING DIRECTOR OR DESIGNEE SHALL BE SUBJECT TO A $9.00 PER SQUARE FOOT MITIGATION FEE.

3. A PRE-CONSTRUCTION MEETING IS REQUIRED PRIOR TO THE ISSUANCE OF GRADING PERMITS. THE DEPARTMENT OF PERMITS, INSPECTION AND ENFORCEMENT, (DPIE) SHALL BE CONTACTED PRIOR TO THE START OF ANY WORK ON THE SITE TO CONDUCT A PRE-CONSTRUCTION MEETING WHERE IMPLEMENTATION OF WOODLAND CONSERVATION MEASURES SHOWN ON THIS PLAN WILL BE DISCUSSED IN DETAIL.

4. THE DEVELOPER OR BUILDER OF THE LOTS OR PARCELS SHOWN ON THIS PLAN SHALL NOTIFY FUTURE BUYERS OF ANY WOODLAND CONSERVATION AREAS THROUGH THE PROVISION OF A COPY OF THIS PLAN AT TIME OF CONTRACT SIGNING. FUTURE PROPERTY OWNERS ARE ALSO SUBJECT TO THIS REQUIREMENT.

5. THE OWNERS OF THE PROPERTY SUBJECT TO THIS TREE CONSERVATION PLAN ARE SOLELY RESPONSIBLE FOR CONFORMANCE TO THE REQUIREMENTS CONTAINED HEREIN.

6. THE PROPERTY IS WITHIN ENVIRONMENTAL STRATEGY AREA ESA-1 AND IS ZONED I-2 (HEAVY INDUSTRIAL).

7. THE SITE IS NOT ADJACENT TO A ROADWAY DESIGNATED AS SCENIC, HISTORIC, A PARKWAY OR A SCENIC BYWAY.

8. THE PROPERTY IS ADJACENT TO GREENBELT ROAD MD-193 WHICH IS CLASSIFIED AS AN ARTERIAL ROADWAY.

9. ALL WOODLANDS DESIGNATED ON THIS PLAN FOR PRESERVATION ARE THE RESPONSIBILITY OF THE PROPERTY OWNER. THE WOODLAND AREAS SHALL REMAIN IN A NATURAL STATE. THIS INCLUDES THE CANOPY TREES AND UNDERSTORY VEGETATION. A REVISED TREE CONSERVATION PLAN IS REQUIRED PRIOR TO CLEARING WOODLAND AREAS THAT ARE NOT SPECIFICALLY IDENTIFIED TO BE CLEARED ON THE APPROVED TCP2.

10. TREE AND WOODLAND CONSERVATION METHODS SUCH AS ROOT PRUNING SHALL BE CONDUCTED AS NOTED ON THIS PLAN.

11. THE LOCATION OF ALL TEMPORARY TREE PROTECTION FENCING (TPFS) SHOWN ON THIS PLAN SHALL BE FLAGGED OR STAKED IN THE FIELD PRIOR TO THE PRE-CONSTRUCTION MEETING. UPON APPROVAL OF THE LOCATIONS BY THE COUNTY INSPECTOR, INSTALLATION OF THE TPFS MAY BEGIN.

12. ALL TEMPORARY TREE PROTECTION FENCING REQUIRED BY THIS PLAN SHALL BE INSTALLED PRIOR TO COMMENCEMENT OF CLEARING AND GRADING OF THE SITE AND SHALL REMAIN IN PLACE UNTIL THE BOND IS RELEASED FOR THE PROJECT. FAILURE TO INSTALL AND MAINTAIN TEMPORARY OR PERMANENT TREE PROTECTIVE DEVICES IS A VIOLATION OF THIS TCP2.

13. THE DEVELOPER AND/OR BUILDER IS RESPONSIBLE FOR THE COMPLETE PRESERVATION OF ALL FORESTED AREAS SHOWN ON THE APPROVED PLAN TO REMAIN UNDISTURBED. ONLY TREES OR PARTS THEREOF DESIGNATED BY THE COUNTY AS DEAD, DYING, OR HAZARDOUS MAY BE REMOVED.

14. A TREE IS CONSIDERED HAZARDOUS IF A CONDITION IS PRESENT WHICH LEADS A CERTIFIED ARBORIST OR LICENSED TREE EXPERT TO BELIEVE THAT THE TREE OR A PORTION OF THE TREE HAS A POTENTIAL TO FALL AND STRIKE A STRUCTURE, PARKING AREA, OR OTHER HIGH USE AREA AND RESULT IN PERSONAL INJURY OR PROPERTY DAMAGE.

15. DURING THE INITIAL STAGES OF CLEARING AND GRADING, IF HAZARDOUS TREES ARE PRESENT, OR TREES ARE PRESENT THAT ARE NOT HAZARDOUS BUT ARE LEANING INTO THE DISTURBED AREA, THE PERMITTEE SHALL REMOVE SAID TREES USING A CHAIN SAW. CORRECTIVE MEASURES REQUIRING THE REMOVAL OF THE HAZARDOUS TREE OR PORTIONS THEREOF SHALL REQUIRE AUTHORIZATION BY THE COUNTY INSPECTOR, ONLY AFTER APPROVAL BY THE INSPECTOR MAY THE TREE BE CUT BY CHAINSAW TO NEAR THE EXISTING GROUND LEVEL. THE STUMP SHALL NOT BE REMOVED OR COVERED WITH SOIL, MULCH OR OTHER MATERIALS THAT WOULD INHIBIT SPROUTING.

16. IF A TREE OR TREES BECOME HAZARDOUS PRIOR TO BOND RELEASE FOR THE PROJECT, DUE TO STORM EVENTS OR OTHER SITUATIONS NOT RESULTING FROM AN ACTION BY THE PERMITTEE, PRIOR TO REMOVAL A CERTIFIED ARBORIST OR A LICENSED TREE EXPERT MUST CERTIFY THAT THE TREE OR THE PORTION OF THE TREE IN QUESTION HAS A POTENTIAL TO FALL AND STRIKE A STRUCTURE, PARKING AREA, OR OTHER HIGH USE AREA AND MAY RESULT IN PERSONAL INJURY OR PROPERTY DAMAGE. IF A TREE OR PORTIONS THEREOF ARE IN IMMINENT DANGER OF STRIKING A STRUCTURE, PARKING AREA, OR OTHER HIGH USE AREA AND MAY RESULT IN PERSONAL INJURY OR PROPERTY DAMAGE THEN THE CERTIFICATION IS NOT REQUIRED AND THE PERMITTEE SHALL TAKE CORRECTIVE ACTION IMMEDIATELY. THE CONDITION OF THE AREA SHALL BE FULLY DOCUMENTED THROUGH PHOTOGRAPHS PRIOR TO CORRECTIVE ACTION BEING TAKEN. THE PHOTOS SHALL BE SUBMITTED TO THE INSPECTOR FOR DOCUMENTATION OF THE DAMAGE.
IF CORRECTIVE PRUNING MAY ALLEVIATE A HAZARDOUS CONDITION, THE CERTIFIED ARBORIST OR A LICENSED TREE EXPERT MAY PROCEED WITHOUT FURTHER AUTHORIZATION. THE PRUNING MUST BE DONE IN ACCORDANCE WITH THE LATEST EDITION OF THE APPROPRIATE ANSI A-300 PRUNING STANDARDS. THE CONDITION OF THE AREA SHALL BE FULLY DOCUMENTED THROUGH PHOTOGRAPHS PRIOR TO CORRECTIVE ACTION BEING TAKEN. THE PHOTOS SHALL BE SUBMITTED TO THE INSPECTOR FOR DOCUMENTATION OF THE DAMAGE.
DEBRIS FROM THE TREE REMOVAL OR PRUNING THAT OCCURS WITHIN 35 FEET OF THE WOODLAND EDGE MAY BE REMOVED AND PROPERLY DISPOSED OF BY RECYCLING, CHIPPING OR OTHER ACCEPTABLE METHODS. ALL DEBRIS THAT IS MORE THAN 35 FEET FROM THE WOODLAND EDGE SHALL BE CUT UP TO ALLOW CONTACT WITH THE GROUND, THUS ENCOURAGING DECOMPOSITION. THE SMALLER MATERIALS SHALL BE PLACED INTO BRUSH PILES THAT WILL SERVE AS WILDLIFE HABITAT.
TREE WORK TO BE COMPLETED WITHIN A ROAD RIGHT-OF-WAY REQUIRES A PERMIT FROM THE MARYLAND DEPARTMENT OF NATURAL RESOURCES UNLESS THE TREE REMOVAL IS SHOWN WITHIN THE APPROVED LIMITS OF DISTURBANCE ON A TCP2, THE WORK IS REQUIRED TO BE CONDUCTED BY A LICENSED TREE EXPERT.

WHEN THE USE OF FEE-IN-LIEU IS PROPOSED:

ALL REQUIRED FEE-IN-LIEU PAYMENTS SHALL BE MADE TO THE WOODLAND CONSERVATION FUND. PROOF OF DEPOSIT SHALL BE PROVIDED PRIOR TO ISSUANCE OF ANY PERMITS RELATED TO THIS TCP2 UNLESS THE PROJECT IS PHASED. PHASED PROJECTS SHALL PAY THE FEE-IN-LIEU AMOUNT FOR EACH PHASE PRIOR TO THE ISSUANCE OF ANY PERMIT FOR THAT PHASE AND SHOWN IN THE FEE-IN-LIEU BREAKDOWN ON THIS TCP2.
WHEN INVASIVE PLANT SPECIES ARE TO BE REMOVED BY THE PERMITTEE:
(USE THE APPLICABLE NOTES BASED ON THE INVASIVE PLANT REMOVAL PLAN)

A. INVASIVE PLANT REMOVAL SHALL BE COMPLETED PRIOR TO (INSERT TIMING MECHANISM) AND CONFORM TO THE RECOMMENDATIONS OF THE INVASIVE PLANT REMOVAL PLAN SHOWN ON THE PLAN PREPARED BY (INSERT THE QUALIFIED PROFESSIONAL'S NAME WHO PREPARED THE INVASIVE PLANT REMOVAL RECOMMENDATIONS) DATED .

B. THE REMOVAL OF NOXIOUS, INVASIVE, AND NON-NATIVES PLANT SPECIES SHALL BE DONE WITH THE USE OF HAND-HELD EQUIPMENT ONLY SUCH AS PRUNERS OR A CHAIN SAW. THESE PLANTS MAY BE CUT NEAR THE GROUND AND THE MATERIAL LESS THAN TWO INCHES DIAMETER MAY BE REMOVED FROM THE AREA AND DISPOSED OF APPROPRIATELY. ALL MATERIAL FROM THESE NOXIOUS, INVASIVE, AND NONNATIVE PLANTS GREATER THAN TWO (2) INCHES DIAMETER SHALL BE CUT TO KNOW CONTACT WITH THE GROUND, THUS ENCOURAGING DECOMPOSITION.

C. THE USE OR BROADCAST SPRAYING OF HERBICIDES IS NOT PERMITTED, HOWEVER, THE USE OF HERBICIDES TO DISCOURAGE RE-SPROUTING OF INVASIVE, NOXIOUS, OR NONNATIVE PLANTS IS PERMITTED IF DONE AS AN APPLICATION OF THE CHEMICAL DIRECTLY TO THE CUT STUMP IMMEDIATELY FOLLOWING CUTTING OF PLANT TOPS. THE USE OF ANY HERBICIDE SHALL BE DONE IN ACCORDANCE WITH THE LABEL INSTRUCTIONS AND BE APPLIED BY A CERTIFIED PESTICIDE APPLICATOR.
WHEN VIRGINIA PINES ARE PRESENT WITHIN 40 FEET OF THE LIMITS OF DISTURBANCE IN A PRESERVATION AREA:

A. THE SUBJECT PROPERTY CONTAINS VIRGINIA PINES (PINUS VIRGINIANA) THAT ARE SUBJECT TO WIND THROW. ALL VIRGINIA PINES GREATER THAN 6 INCHES IN DIAMETER WITHIN 40 FEET OF THE FINAL PROPOSED LIMIT OF DISTURBANCE OR THE BOUNDARY OF THE PROPERTY SHALL BE CUT DOWN BY HAND DURING THE CLEARING OF THE SITE.

B. AFTER THE VIRGINIA PINES HAVE BEEN REMOVED, THE CONTRACTOR RESPONSIBLE FOR IMPLEMENTATION OF THIS TCP2 SHALL SUBMIT AN EVALUATION OF THE STOCKING LEVELS FOR THE RESIDUAL STAND. MANAGEMENT TECHNIQUES TO BE APPLIED TO THE RESIDUAL STAND, AND SUPPLEMENTAL PLANTING REQUIREMENTS TO THE M-NCPPC PLANNING DEPARTMENT. THIS EVALUATION SHALL BE SUBMITTED PRIOR TO THE ISSUANCE OF THE FIRST BUILDING PERMIT TO ENSURE THAT ALL HIGH RISK TREES HAVE BEEN REMOVED. A PLANTING SCHEDULE AND/OR DETAILS FOR THE MANAGEMENT OF NATURAL REGENERATION TO FULLY RESTOCK THE SITE MUST BE SHOWN ON THE PLAN.

POST DEVELOPMENT NOTES

A. IF THE DEVELOPER OR BUILDER NO LONGER HAS AN INTEREST IN THE PROPERTY AND THE NEW OWNER DESIRES TO REMOVE A HAZARDOUS TREE OR PORTION THEREOF, THE NEW OWNER SHALL OBTAIN A WRITTEN STATEMENT FROM A CERTIFIED ARBORIST OR LICENSED TREE EXPERT IDENTIFYING THE HAZARDOUS CONDITION AND THE PROPOSED CORRECTIVE MEASURES PRIOR TO HAVING THE WORK CONDUCTED. AFTER PROPER DOCUMENTATION HAS BEEN COMPLETED PER THE HANDOUT "GUIDANCE FOR PRINCE GEORGE'S COUNTY PROPERTY OWNERS, PRESERVATION OF WOODLAND CONSERVATION AREAS", THE ARBORIST OR TREE EXPERT MAY THEN REMOVE THE TREE. THE STUMP SHALL BE CUT AS CLOSE TO THE GROUND AS POSSIBLE AND LEFT IN PLACE. THE REMOVAL OR GRINDING OF THE STUMPS IN THE WOODLAND CONSERVATION AREA IS NOT PERMITTED.
IF A TREE OR PORTIONS THEREOF ARE IN IMMINENT DANGER OF STRIKING A STRUCTURE, PARKING AREA, OR OTHER HIGH USE AREA AND MAY RESULT IN PERSONAL INJURY OR PROPERTY DAMAGE THEN THE CERTIFICATION IS NOT REQUIRED AND THE PERMITEE SHALL TAKE CORRECTIVE ACTION IMMEDIATELY. THE CONDITION OF THE AREA SHALL BE FULLY DOCUMENTED THROUGH PHOTOGRAPHS PRIOR TO CORRECTIVE ACTION BEING TAKEN. THE PHOTOS SHALL BE SUBMITTED TO THE INSPECTOR FOR DOCUMENTATION OF THE DAMAGE.
TREE WORK TO BE COMPLETED WITHIN A ROAD RIGHT-OF-WAY REQUIRES A PERMIT FROM THE MARYLAND DEPARTMENT OF NATURAL RESOURCES UNLESS THE TREE REMOVAL IS SHOWN WITHIN THE APPROVED LIMITS OF DISTURBANCE ON A TCP2, THE WORK IS REQUIRED TO BE CONDUCTED BY A LICENSED TREE EXPERT.

B. THE REMOVAL OF NOXIOUS, INVASIVE, AND NON-NATIVE PLANT SPECIES FROM ANY WOODLAND PRESERVATION AREA SHALL BE DONE WITH THE USE OF HAND-HELD EQUIPMENT ONLY (PRUNERS OR A CHAIN SAW). THESE PLANTS MAY BE CUT NEAR THE GROUND AND MATERIAL LESS THAN TWO INCHES DIAMETER MAY BE REMOVED FROM THE AREA AND DISPOSED OF APPROPRIATELY. ALL MATERIAL FROM THESE NOXIOUS, INVASIVE, AND NON-NATIVE PLANTS GREATER THAN TWO (2) INCHES DIAMETER SHALL BE CUT TO ALLOW CONTACT WITH THE GROUND, THUS ENCOURAGING DECOMPOSITION.

C. THE USE OF BROADCAST SPRAYING OF HERBICIDES IS NOT PERMITTED, HOWEVER, THE USE OF HERBICIDES TO DISCOURAGE RE-SPROUTING OF INVASIVE, NOXIOUS, OR NON-NATIVE PLANTS IS PERMITTED IF DONE AS AN APPLICATION OF THE CHEMICAL DIRECTLY TO THE CUT STUMP IMMEDIATELY FOLLOWING CUTTING OF PLANT TOPS. THE USE OF ANY HERBICIDE SHALL BE DONE IN ACCORDANCE WITH THE LABEL INSTRUCTIONS.

D. THE USE OF CHAINSAWS IS EXTREMELY DANGEROUS AND SHOULD NOT BE CONDUCTED WITH POORLY MAINTAINED EQUIPMENT, WITHOUT SAFETY EQUIPMENT, OR BY INDIVIDUALS NOT TRAINED IN THE USE OF THIS EQUIPMENT FOR THE PRUNING AND/OR CUTTING OF TREES.
PROTECTION OF REFORESTATION AND AFFORESTATION AREAS BY INDIVIDUAL HOMEOWNERS

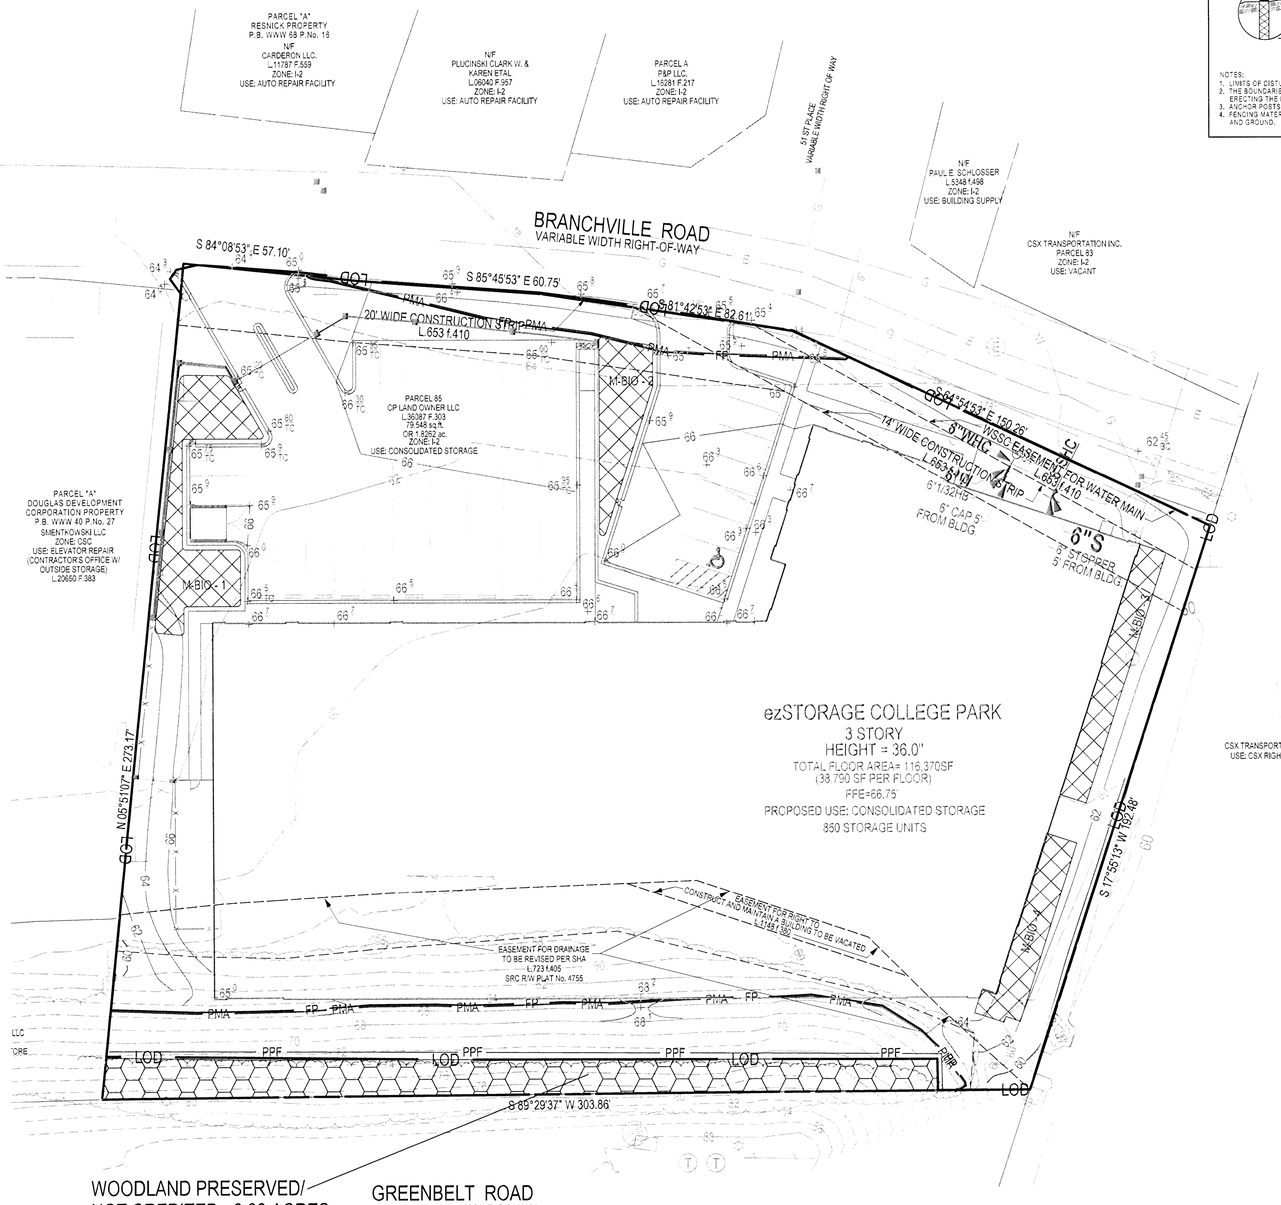

TPDG
OPTION 3

TREE PROTECTIVE DEVICE
BLAZE ORANGE PLASTIC MESH

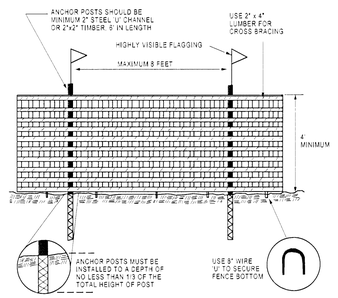

NOTES:
1. LIMITS OF DISTURBANCE WILL BE SET AS PART OF THE REVIEW PROCESS FOR AN APPROVED TCP.
2. THE BOUNDARIES OF THE LIMITS OF DISTURBANCE SHOULD BE STAKED AND FLAGGED PRIOR TO ERECTING THE PROTECTIVE DEVICE.
3. ANCHOR POSTS SHOULD BE PLACED TO AVOID SEVERING OR DAMAGING LARGE TREE ROOTS.
4. FENCING MATERIAL SHOULD BE FASTENED SECURELY TO THE ANCHOR POSTS, CROSS BRACING, AND GROUND.

Standard Woodland Conservation Worksheet for Prince George's County

SECTION I - Establishing Site Information - (Enter acres for each zone)

1 Zone	I-2			
2 Gross Tract	7.92			
3 Floodplain	1.69			
4 Previously Dedicated Land	0.00			
5 Net Tract (NTA)	6.23	3.00	3.00	

		Revision #	0
6 TCP# Number			
7 Property Description or Subdivision Name	ezStorage College Park		
8 Is this site subject to the 1989 Ordinance? (Y/N)	N		
9 Is this site in the Patuxent? (Y/N)	N		
10 Are there prior TCP approvals which include a combination of the above? (Y/N)	N		
11 Is any portion of the property in a WC Bank?	N		
12 Is any portion of the property in a WC Bank?			
13 Break-even Point (preservation) =	3.06	acres	
14 Clearing permitted w/o reforestation =	3.12	acres	

SECTION II - Determining Requirements - (Enter acres for each corresponding column)

	Column A WCT-APT =	Column B Net Tract	Column C Floodplain (1:1)	Column D Off-Site Impacts (1:1)
15 Existing Woodland		0.18	0.10	
16 Woodland Conservation Threshold (WCT) =	15.00%	0.93		
17 Smaller of 15 or 14		0.93		
18 Woodland above WCT		0.00		
19 Woodland cleared		0.10	0.10	
20 Woodland preserved above WCT (smaller of 18 or 17)		0.00		
21 Clearing above WCT (1.25 :1) replacement requirement		0.00		
22 Woodland cleared below WCT		0.00		
23 Clearing below WCT (2.5 :1 replacement requirement)		0.00		
24 Reforestation Required Threshold (APT) =	15.00%	0.00		
25 Off-site WCA preservation being provided on this property		0.00		
26 Woodland Conservation Required		0.10	acres	

SECTION III - Meeting the Requirements - (Enter acres for each corresponding column)

27 Woodland Preservation		0.00		
28 Reforestation / Reforestation		0.00	Bond amount	$ -
29 Natural Regeneration		0.00		
30 Landscape Credits		0.00		
31 Specimen Habitat Tree Credit (CRZ area * 2.5)	0.00			
32 Forest Enhancement Credit (Area * .25)	0.00			
33 Street Tree Credit (Existing or 10 year canopy coverage)		0.00		
34 Area approved for fee-in-lieu PFA		0.10	Fee amount	$6,272.64
35 Area approved for fee-in-lieu non PFA		0.00	Fee amount	$0.00
36 Off-site Woodland Conservation Credits Required		0.00		
37 Off-site WCA preservation being provided on this property		0.00		
38 Off-site WCA afforestation being provided on this property		0.00		
39 Woodland Conservation Provided		0.10	acres	

40 Area of woodland not cleared	0.08	acres
41 Non-tract woodland retained not part of requirements	0.08	acres
42 100-floodplain woodland retained	0.00	acres
43 Off-site woodland conservation provided	0.00	acres
44 Off-site woodland retained not credited	0.08	acres

45 Prepared by: David Bickel — Signed — 3-28-17 — Date

LEGEND

- EXISTING TREE LINE
- PMA — PATUXENT MANAGEMENT AREA
- FP — 100 YEAR FLOODPLAIN LIMITS (SOURCE: ANACOSTIA RIVER WATERSHED STUDY, PLATE M-5)
- WOODLAND PRESERVED - NOT CREDITED
- PROPERTY BOUNDARY
- LOD — PROPERTY BOUNDARY
- EASEMENT
- EXISTING CONTOUR
- 64 — PROPOSED CONTOUR
- PPF — TREE PROTECTION FENCE

Prince George's County Planning Department, M-NCPPC
Environmental Planning Section
TREE CONSERVATION PLAN APPROVAL
TCP2-020-2016

#	APPROVED BY	DATE	DRD CASE
00	Maria Finn	9/9/2017	DSP-15031
01			
02			
03			
04			
05			

THIS BLOCK IS FOR OFFICIAL USE ONLY
QR label certifies that this plan meets conditions of final approval by the Planning Board, its designee or the District Council.
M-NCPPC
APPROVAL

PROJECT NAME: ezStorage College Park
PROJECT NUMBER: DSP-15031
For Conditions of Approval see Site Plan Cover Sheet or Approval Sheet. Revision numbers must be included in the Project Number.

SOLTESZ

Engineering
Surveying
Planning
Environmental Sciences

LANHAM OFFICE
4300 Forbes Boulevard, Suite 230
Lanham, MD 20706
P. 301.794.7555 F. 301.794.7656
www.soltesco.com

Rockville
Lanham
Waldorf
Leonardtown
Frederick
Soltesz DC, LLC

NO.	REVISIONS	BY	DATE
DATE: AUGUST 2015	CAD STANDARDS VERSION: VA - 2009		
DESIGNED: BCG	TECHNICIAN: BCG	CHECKED: THD	

MISS UTILITY NOTE
INFORMATION CONCERNING EXISTING UNDERGROUND UTILITIES WAS OBTAINED FROM AVAILABLE RECORDS. THE CONTRACTOR MUST DETERMINE THE EXACT LOCATION AND ELEVATION OF ALL EXISTING UTILITIES AND UTILITY CROSSINGS BY DIGGING TEST PITS BY HAND, WELL IN ADVANCE OF THE START OF EXCAVATION. CONTACT "MISS UTILITY AT 1-800-257-7777, 48 HOURS PRIOR TO THE START OF EXCAVATION. IF CLEARANCES ARE LESS THAN SHOWN ON THIS PLAN OR TWELVE (12) INCHES, WHICHEVER IS LESS, CONTACT THE ENGINEER AND THE UTILITY COMPANY BEFORE PROCEEDING WITH CONSTRUCTION. CLEARANCES LESS THAN NOTED MAY REQUIRE REVISIONS TO THIS PLAN.

OWNER/DEVELOPER/APPLICANT
SIENA CORPORATION
8221 SNOWDEN RIVER PARKWAY
COLUMBIA, MARYLAND 21045
OFFICE: (443) 539-3070
CONTACT NAME: CRAIG PITTINGER

MAP ____ GRID ____
TAX MAP: 25, F4 — ZONING CATEGORY: I-2
WSSC 200' SHEET: 210NE05
SITE DATUM
HORIZONTAL: NAD 83
VERTICAL: NGVD29

STATE OF MARYLAND — DAVID WAYNE BICKEL — 21397 — REGISTERED LANDSCAPE ARCHITECT

TREE CONSERVATION PLAN - TYPE 2

EZ STORAGE COLLEGE PARK
5151 BRANCHVILLE ROAD
COLLEGE PARK, MARYLAND
BERWIN (21ST) ELECTION DISTRICT, PRINCE GEORGE'S COUNTY

1" = 22'
SHEET 1 OF 1
PROJECT NO. 15770690

The original of this drawing document was prepared by Soltesz, Inc. (SOLTESZ). If this document was not obtained directly from SOLTESZ and/or it was transmitted electronically, SOLTESZ cannot guarantee that unauthorized changes and / or alterations were not made by others. If verification of this information contained herein is needed, contact should be made directly with SOLTESZ and/or it was transmitted electronically, SOLTESZ makes no warranties, express or implied, concerning the accuracy of any information that has been transmitted by electronic means.

P:\15770600\ENGINEER\ENVTCP\Plt.sht Scale= 20.0000 ft / in. User= jroh PLTdrv= PDF_Grey_150.pltcfg PrintBar= TEXT_SUB.tbl 3/28/2017 10:22:05 AM
